

Shoalhaven Hospital Redevelopment

Dust Monitoring Report 19

Project ID	20230220.8
Document Title	Dust Monitoring Report 19
Attention To	John Holland Group Pty Ltd

Revision	Date	Document Reference	Prepared By	Checked By	Approved By
0	17/12/2024	20230220.8/1712A/R0/HD	HD		TB

TABLE OF CONTENTS

1	INTRODUCTION	4
2	SITE DESCRIPTION	4
2.1.1	Surrounding Receivers.....	4
3	MONITORING LOCATIONS AND DESCRIPTION	6
3.1	MONITORING PERIOD	9
3.2	MONITORING EQUIPMENT	9
4	DUST MONITORING	9
4.1	PROJECT DOCUMENTATION	9
4.1.1	Dust Management Levels	9
4.2	MONITORED DUST LEVELS	10
4.2.1	East Boundary Facing Shoalhaven Street (Monitor HEX-000171).....	11
4.2.2	North Boundary Facing Block A & B (Monitor HEX-000130).....	12
4.2.3	West of Early Works Zone (Monitor HEX-000232).....	13
4.2.4	Pre-School Boundary (Monitor HEX-000592).....	14
4.2.5	Near ICU and Loading Dock (Monitor HEX-000733)	15
4.3	DISCUSSION	16
4.3.1	East Boundary Opposite Shoalhaven Street Residences (HEX-000171)	16
4.3.2	North Boundary Near Block A and B (HEX-000130).....	16
4.3.3	West of Early Works Zone Near Block A (HEX-000232).....	16
4.3.4	Pre-School Boundary Near Outdoor Play Area (HEX-000592).....	16
4.3.5	Near ICU and Loading Dock (HEX-000733)	16
4.4	MANAGEMENT OF DUST LEVELS	17
5	CONCLUSION.....	18
	APPENDIX A – DUST MONITORING GRAPHS	19

1 INTRODUCTION

This report presents the results of dust monitoring conducted by Acoustic Logic for the Shoalhaven Hospital Redevelopment project site. Details presented in this report include monitoring locations, relevant project objectives, measured levels over the monitoring period and discussion of results.

This report presents the results of monitoring for the month of December between 1/12/2024 and 19/12/2024. Monitoring has been ongoing since 29th May 2023.

This report should be read in conjunction with the Construction Noise, Dust and Vibration Management Sub Plan prepared by this office (ref: 20230220.1/0506A/R1/VF, dated 05/06/2023)

2 SITE DESCRIPTION

The project site is located at Shoalhaven Hospital Redevelopment. Site works are now at the building construction stage.

2.1.1 Surrounding Receivers

Based on site investigations, the following developments surround the site:

Table 1 – Sensitive Receivers

Receiver (Refer Figure 1)	Receiver Type	Comment
R1	Residential	Detached dwellings to south of North Street, and residences and St Michaels Catholic Church and school to the east.
R2	Residential	Detached dwellings to north east, opposite Shoalhaven Street with some health and commercial and recreational uses.
PS	School	Shoalhaven Community Pre-School (future relocated site).
CC	Hospital	Cancer Centre overnight accommodation (part of the greater hospital site).

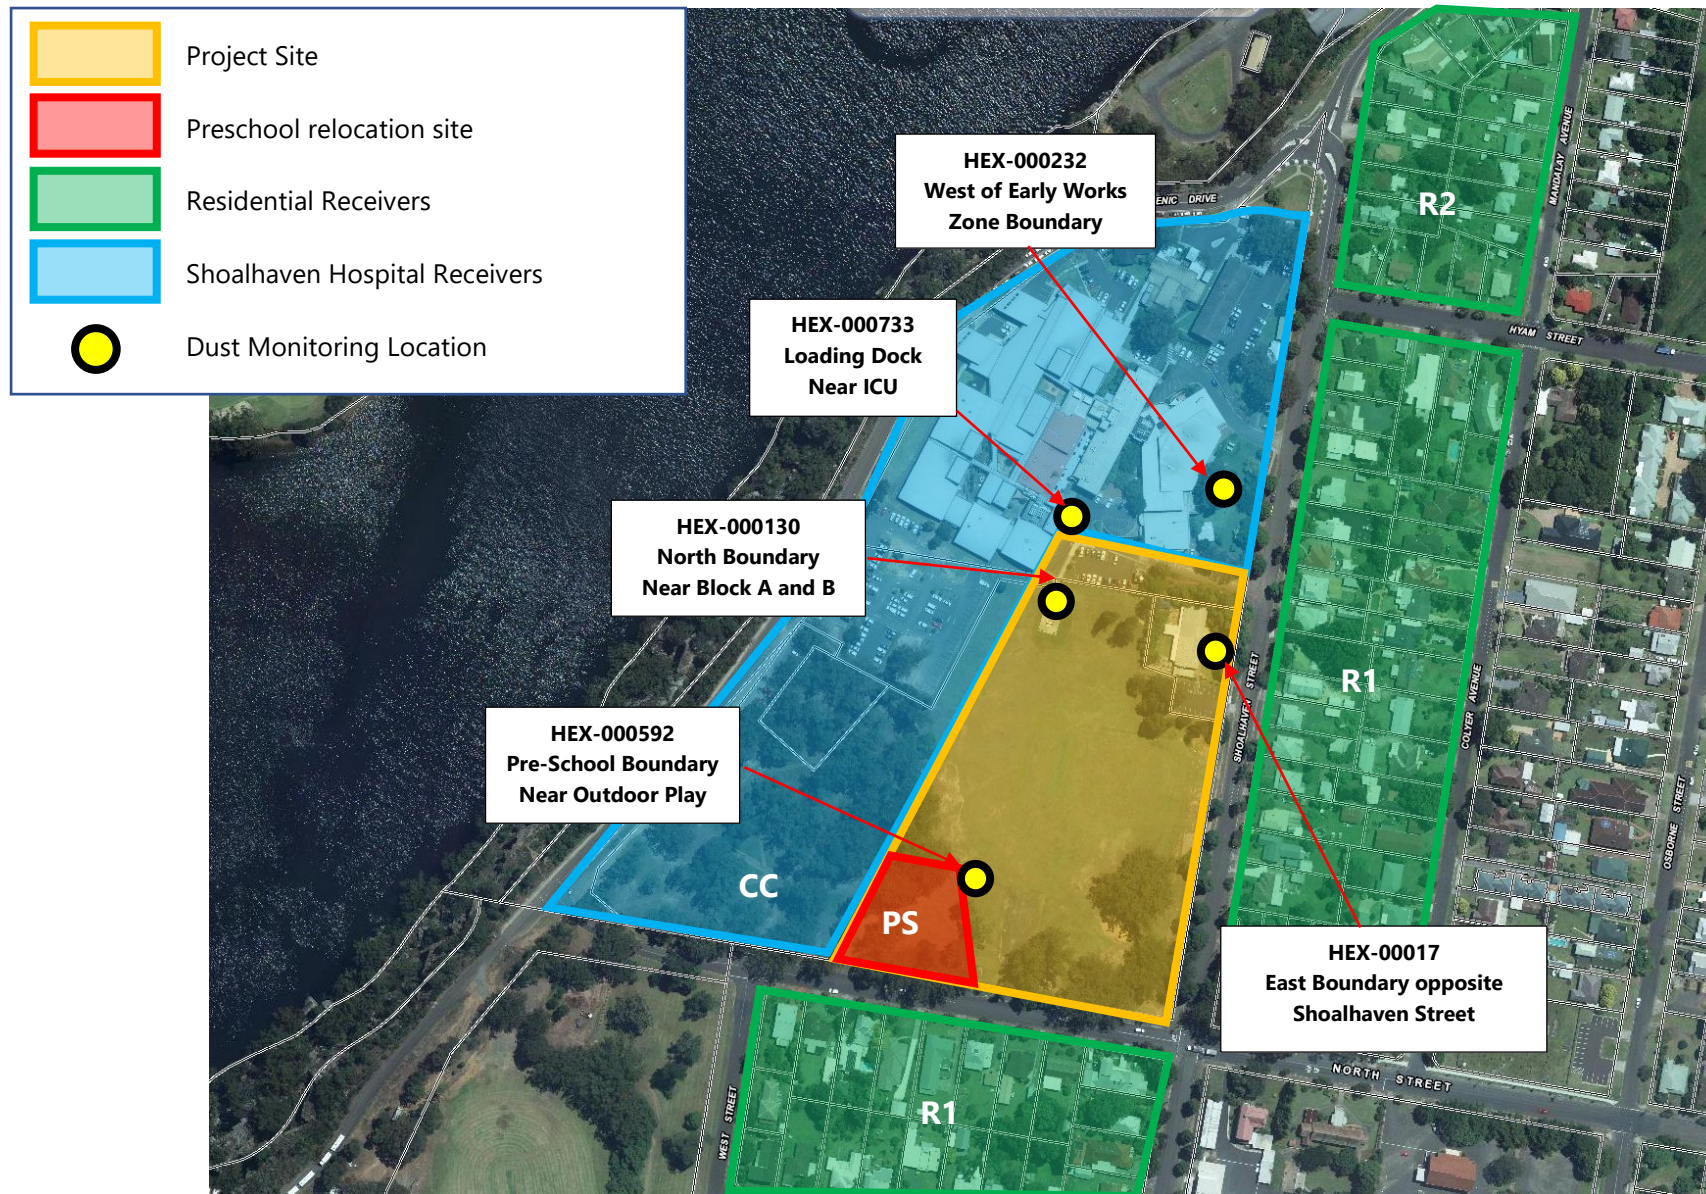


Figure 1 – Site Map. Monitoring Locations and Surrounding Receivers

3 MONITORING LOCATIONS AND DESCRIPTION

Refer to Figure 1 and photos below for monitoring locations.



**Figure 2 – HEX000171 --East Boundary Opposite Shoalhaven Street (left) and
HEX000131 – North Boundary Near Block A and B (right)**



Figure 3 – HEX000232 – West of Early Works Zone Near Block A



Figure 4 – HEX000592 – Pre-School Boundary Fence Near Outdoor Play Area



Figure 5 – HEX000733 – Near ICU and Loading Dock

3.1 MONITORING PERIOD

This report presents the results of monitoring between 1/12/2024 and 19/12/2024.

Monitoring has been ongoing since 29th May 2023.

3.2 MONITORING EQUIPMENT

Dust monitoring was conducted using SiteHive Hexanode monitors. Monitors are programmed to continuously store noise data over every 15-minute period

4 DUST MONITORING

4.1 PROJECT DOCUMENTATION

Construction impacts to nearby development have been determined in the Construction Noise, Dust and Vibration Management Sub Plan (ref: 20230220.1/0506A/R1/VF, dated 05/06/2023)

4.1.1 Dust Management Levels

Dust monitoring is conducted to measure mechanically generated respirable PM₁₀ dust particles (< 10µm) and PM_{2.5} dust particles (< 2.5µm), which are generally understood to be the main health concern in airborne dust. The air quality limits are based on the standards outlined in Department of the Environment's *National Environment Protection (Ambient Air Quality) Measure* and NSW EPA's air quality categories.

It should be noted that the dust monitoring results can be influenced by events such as fires, fogs and dust storms, thus the PM₁₀ limit has an allowance of 5 days per year to account for the effects of these two effects. It is noted that site dust suppression systems using fine water sprays can affect the dust count of laser-based measurement systems and so too can pollen in Spring. The PM₁₀ and PM_{2.5} goals are summarised below.

Table 2 – PM₁₀ and PM_{2.5} Goals (24-Hour Average)

Pollutant	Averaging Time	Maximum Concentration
Particulate Matter PM ₁₀	24 hours	50 µg/m ³
Particulate Matter PM _{2.5}	24 hours	25 µg/m ³

The EPA has air quality categories based on particle concentration over a one-hour average. These levels may be used to control site dust emissions. Typically, a project alert trigger level is set on the 'Poor' category level. **However, the assessment level is based on the 24-hour average.**

Table 3 – PM₁₀ and PM_{2.5} Goals (1-Hour Average)

Pollutant	Air Quality Category (AQC)				
	Good	Fair	Poor	Very Poor	Extremely Poor
Particulate Matter PM ₁₀ (µg/m ³)	< 50	50-100	100-200	200-600	600 and above
Particulate Matter PM _{2.5} (µg/m ³)	< 25	25-50	50-100	100-300	300 and above

4.2 MONITORED DUST LEVELS

The following legend has been generated with reference to exceedances within the monitored dust levels as follows and applied to the tables below.

RED = CONSTRUCTION RELATED EXCEEDANCE

BLUE = EXCEEDANCES DURING WEATHER AFFECTED PERIODS

GREY = EXCEEDANCES DURING OUT OF HOURS

Where true exceedances are recorded, additional analysis has been provided in the discussion below.

4.2.1 East Boundary Facing Shoalhaven Street (Monitor HEX-000171)

The daily average PM_{2.5} and PM₁₀ concentration levels are presented below:

Table 4 – East Boundary (HEX-000171) Daily Average PM₁₀ and PM_{2.5} Concentration

Date	24hr Average PM _{2.5} and PM ₁₀ Concentration					
	PM _{2.5} Level (µg/m ³)	PM _{2.5} Limit (µg/m ³)	Compliance	PM ₁₀ Level (µg/m ³)	PM ₁₀ Limit (µg/m ³)	Compliance
1/12/2024	13	25	Yes	57	50	Yes
2/12/2024	5		Yes	27		Yes
3/12/2024	5		Yes	23		Yes
4/12/2024	17		Yes	54		Yes
5/12/2024	19		Yes	63		Yes
6/12/2024	15		Yes	47		Yes
7/12/2024	7		Yes	23		Yes
8/12/2024	20		Yes	66		Yes
9/12/2024	23		Yes	77		Yes
10/12/2024	15		Yes	53		Yes
11/12/2024	11		Yes	39		Yes
12/12/2024	14		Yes	52		Yes
13/12/2024	15		Yes	57		Yes
14/12/2024	12		Yes	48		Yes
15/12/2024	13		Yes	42		Yes
16/12/2024	12		Yes	41		Yes
17/12/2024	17		Yes	61		Yes
18/12/2024	17		Yes	62		Yes
19/12/2024	13		Yes	47		Yes

RED = CONSTRUCTION RELATED EXCEEDANCE

BLUE = COMPLIES - EXCEEDANCES DURING WEATHER AFFECTED PERIODS

GREY = COMPLIES - EXCEEDANCES DURING OUT OF HOURS

4.2.2 North Boundary Facing Block A & B (Monitor HEX-000130)

The daily average PM_{2.5} and PM₁₀ concentration levels are presented below:

Table 5 – North Boundary (HEX-000130) Daily Average PM₁₀ and PM_{2.5} Concentration

Date	24hr Average PM _{2.5} and PM ₁₀ Concentration					
	PM _{2.5} Level (µg/m ³)	PM _{2.5} Limit (µg/m ³)	Compliance	PM ₁₀ Level (µg/m ³)	PM ₁₀ Limit (µg/m ³)	Compliance
1/12/2024	11	25	Yes	44	50	Yes
2/12/2024	5		Yes	25		Yes
3/12/2024	5		Yes	29		Yes
4/12/2024	14		Yes	50		Yes
5/12/2024	6		Yes	38		Yes
6/12/2024	3		Yes	53		Yes
7/12/2024	1		Yes	35		Yes
8/12/2024	1		Yes	26		Yes
9/12/2024	2		Yes	43		Yes
10/12/2024	3		Yes	53		Yes
11/12/2024	2		Yes	44		Yes
12/12/2024	1		Yes	39		Yes
13/12/2024	1		Yes	39		Yes
14/12/2024	1		Yes	64		Yes
15/12/2024	1		Yes	108		Yes
16/12/2024	1		Yes	94		Yes
17/12/2024	1		Yes	72		Yes
18/12/2024	2		Yes	60		Yes
19/12/2024	2		Yes	48		Yes

RED = CONSTRUCTION RELATED EXCEEDANCE

BLUE = COMPLIES - EXCEEDANCES DURING WEATHER AFFECTED PERIODS

GREY = COMPLIES - EXCEEDANCES DURING OUT OF HOURS

4.2.3 West of Early Works Zone (Monitor HEX-000232)

The daily average PM_{2.5} and PM₁₀ concentration levels are presented below:

Table 6 – West of Early Works (HEX-000232) Daily Average PM₁₀ and PM_{2.5} Concentration

Date	24hr Average PM _{2.5} and PM ₁₀ Concentration					
	PM _{2.5} Level (µg/m³)	PM _{2.5} Limit (µg/m³)	Compliance	PM ₁₀ Level (µg/m³)	PM ₁₀ Limit (µg/m³)	Compliance
1/12/2024	9	25	Yes	42	50	Yes
2/12/2024	4		Yes	17		Yes
3/12/2024	4		Yes	15		Yes
4/12/2024	12		Yes	31		Yes
5/12/2024	13		Yes	35		Yes
6/12/2024	8		Yes	23		Yes
7/12/2024	4		Yes	12		Yes
8/12/2024	14		Yes	42		Yes
9/12/2024	16		Yes	45		Yes
10/12/2024	10		Yes	33		Yes
11/12/2024	8		Yes	21		Yes
12/12/2024	6		Yes	21		Yes
13/12/2024	9		Yes	30		Yes
14/12/2024	9		Yes	30		Yes
15/12/2024	9		Yes	28		Yes
16/12/2024	7		Yes	20		Yes
17/12/2024	12		Yes	37		Yes
18/12/2024	12		Yes	37		Yes
19/12/2024	8		Yes	26		Yes

RED = CONSTRUCTION RELATED EXCEEDANCE

BLUE = COMPLIES - EXCEEDANCES DURING WEATHER AFFECTED PERIODS

GREY = COMPLIES - EXCEEDANCES DURING OUT OF HOURS

4.2.4 Pre-School Boundary (Monitor HEX-000592)

The daily average PM_{2.5} and PM₁₀ concentration levels are presented below:

Table 7 – Pre-School Boundary (HEX-000592) Daily Average PM₁₀ and PM_{2.5} Concentration

Date	24hr Average PM _{2.5} and PM ₁₀ Concentration					
	PM _{2.5} Level (µg/m ³)	PM _{2.5} Limit (µg/m ³)	Compliance	PM ₁₀ Level (µg/m ³)	PM ₁₀ Limit (µg/m ³)	Compliance
1/12/2024	6	25	Yes	35	50	Yes
2/12/2024	3		Yes	13		Yes
3/12/2024	3		Yes	11		Yes
4/12/2024	9		Yes	29		Yes
5/12/2024	11		Yes	34		Yes
6/12/2024	7		Yes	23		Yes
7/12/2024	3		Yes	10		Yes
8/12/2024	11		Yes	35		Yes
9/12/2024	12		Yes	37		Yes
10/12/2024	7		Yes	23		Yes
11/12/2024	6		Yes	21		Yes
12/12/2024	5		Yes	19		Yes
13/12/2024	7		Yes	27		Yes
14/12/2024	7		Yes	23		Yes
15/12/2024	7		Yes	19		Yes
16/12/2024	6		Yes	25		Yes
17/12/2024	9		Yes	30		Yes
18/12/2024	9		Yes	29		Yes
19/12/2024	6		Yes	21		Yes

RED = CONSTRUCTION RELATED EXCEEDANCE

BLUE = COMPLIES - EXCEEDANCES DURING WEATHER AFFECTED PERIODS

GREY = COMPLIES - EXCEEDANCES DURING OUT OF HOURS

4.2.5 Near ICU and Loading Dock (Monitor HEX-000733)

The daily average PM_{2.5} and PM₁₀ concentration levels are presented below:

Table 8 – ICU and Loading Dock (HEX-000733) Daily Average PM₁₀ and PM_{2.5} Concentration

Date	24hr Average PM _{2.5} and PM ₁₀ Concentration					
	PM _{2.5} Level (µg/m³)	PM _{2.5} Limit (µg/m³)	Compliance	PM ₁₀ Level (µg/m³)	PM ₁₀ Limit (µg/m³)	Compliance
5/12/2024	8	25	Yes	22	50	Yes
6/12/2024	7		Yes	26		Yes
7/12/2024	4		Yes	12		Yes
8/12/2024	12		Yes	36		Yes
9/12/2024	13		Yes	42		Yes
10/12/2024	9		Yes	30		Yes
11/12/2024	7		Yes	20		Yes
12/12/2024	6		Yes	21		Yes
13/12/2024	8		Yes	35		Yes
14/12/2024	8		Yes	26		Yes
15/12/2024	8		Yes	23		Yes
16/12/2024	6		Yes	20		Yes
17/12/2024	11		Yes	38		Yes
18/12/2024	11		Yes	41		Yes
19/12/2024	7		Yes	28		Yes

RED = CONSTRUCTION RELATED EXCEEDANCE

BLUE = COMPLIES - EXCEEDANCES DURING WEATHER AFFECTED PERIODS

GREY = COMPLIES - EXCEEDANCES DURING OUT OF HOURS

Note: The monitor was installed on Thursday 5th of December.

4.3 DISCUSSION

4.3.1 East Boundary Opposite Shoalhaven Street Residences (HEX-000171)

- During the monitoring period, PM_{2.5} dust levels at the monitoring location were found to be within the maximum concentration permitted by Department of the Environment's *National Environment Protection (Ambient Air Quality) Measure*.
- During the monitoring period, PM₁₀ dust levels at the monitoring location were found to be within the maximum concentration permitted by Department of the Environment's *National Environment Protection (Ambient Air Quality) Measure*.

4.3.2 North Boundary Near Block A and B (HEX-000130)

- During the monitoring period, PM_{2.5} dust levels at the monitoring location were found to be within the maximum concentration permitted by Department of the Environment's *National Environment Protection (Ambient Air Quality) Measure*.
- During the monitoring period, PM₁₀ dust levels at the monitoring location were found to be within the maximum concentration permitted by Department of the Environment's *National Environment Protection (Ambient Air Quality) Measure*.

4.3.3 West of Early Works Zone Near Block A (HEX-000232)

- During the monitoring period, PM_{2.5} dust levels at the monitoring location were found to be within the maximum concentration permitted by Department of the Environment's *National Environment Protection (Ambient Air Quality) Measure*.
- During the monitoring period, PM₁₀ dust levels at the monitoring location were generally found to be within the maximum concentration permitted by Department of the Environment's *National Environment Protection (Ambient Air Quality) Measure*.

4.3.4 Pre-School Boundary Near Outdoor Play Area (HEX-000592)

- During the monitoring period, PM_{2.5} dust levels at the monitoring location were found to be within the maximum concentration permitted by Department of the Environment's *National Environment Protection (Ambient Air Quality) Measure*.
- During the monitoring period, PM₁₀ dust levels at the monitoring location were generally found to be within the maximum concentration permitted by Department of the Environment's *National Environment Protection (Ambient Air Quality) Measure*.

4.3.5 Near ICU and Loading Dock (HEX-000733)

- During the monitoring period, PM_{2.5} dust levels at the monitoring location were found to be within the maximum concentration permitted by Department of the Environment's *National Environment Protection (Ambient Air Quality) Measure*.
- During the monitoring period, PM₁₀ dust levels at the monitoring location were generally found to be within the maximum concentration permitted by Department of the Environment's *National Environment Protection (Ambient Air Quality) Measure*.

4.4 MANAGEMENT OF DUST LEVELS

General Notes:

- It should be noted that the measured dust levels will also be affected by meteorological events outside the project site, such as heavy rain and wind, high humidity, dust storms, bush fires, high pollen count and the like.

Response to Exceedances

The general response procedures adopted by JH are as follows:

- The project team is notified via SMS alert messages when hourly average dust levels are exceeded
- Methodology and works across the project site and near to the specific monitoring location are recorded.
- Where monitoring locations are confirmed to be potentially impacted by the adjacent works (i.e., where exceedance notifications are received but no works are occurring near to the monitoring location – indicating alerts are as a result of external impacts – refer general notes in Section 4.3.4), work methodology was investigated and mistor(s) are deployed.

Acoustic Logic confirms JH has implemented best practices as well as reasonable and feasible mitigation measures in response to dust exceedances over the majority of this monitoring period.

A review of works on the days that led to exceedance of dust levels should be carried out and the following additional recommendations for ongoing dust management should be implemented:

- Loose soil and/or dusty stockpiles should be covered with tarpaulin/plastic sheeting outside of working hours and during extended periods where not in use.
- Minimisation/relocation of stockpiles away from dust-sensitive receivers to minimise potential for disturbance due to prevailing winds.
- Additional dust suppression methods such as directed water sprays directly onto excavation equipment and work areas should be implemented where alternative methodology cannot be found.

5 CONCLUSION

Dust monitoring has been conducted at different locations for the Shoalhaven Hospital Redevelopment between 1/12/2024 and 19/12/2024. For this monitoring period, we note the following:

- Hexanode HEX-000171 at the East Boundary - PM_{2.5} and PM₁₀ dust levels were generally within the criteria during this monitoring period.
- Hexanode HEX-000130 at the North Boundary - PM_{2.5} and PM₁₀ dust levels were generally within the criteria during this monitoring period.
- Hexanode HEX-000232 at the West of Early Works Zone - PM_{2.5} and PM₁₀ dust levels were generally within the criteria during this monitoring period.
- Hexanode HEX-000592 at the Preschool - PM_{2.5} and PM₁₀ dust levels were generally within the criteria during this monitoring period.
- Hexanode HEX-000733 Near the ICU and Loading Dock - PM_{2.5} and PM₁₀ dust levels were generally within the criteria during this monitoring period.



We trust this information is satisfactory. Please contact us should you have any further queries.



Yours faithfully,




Acoustic Logic Pty Ltd
Hyde Deng

APPENDIX A – DUST MONITORING GRAPHS

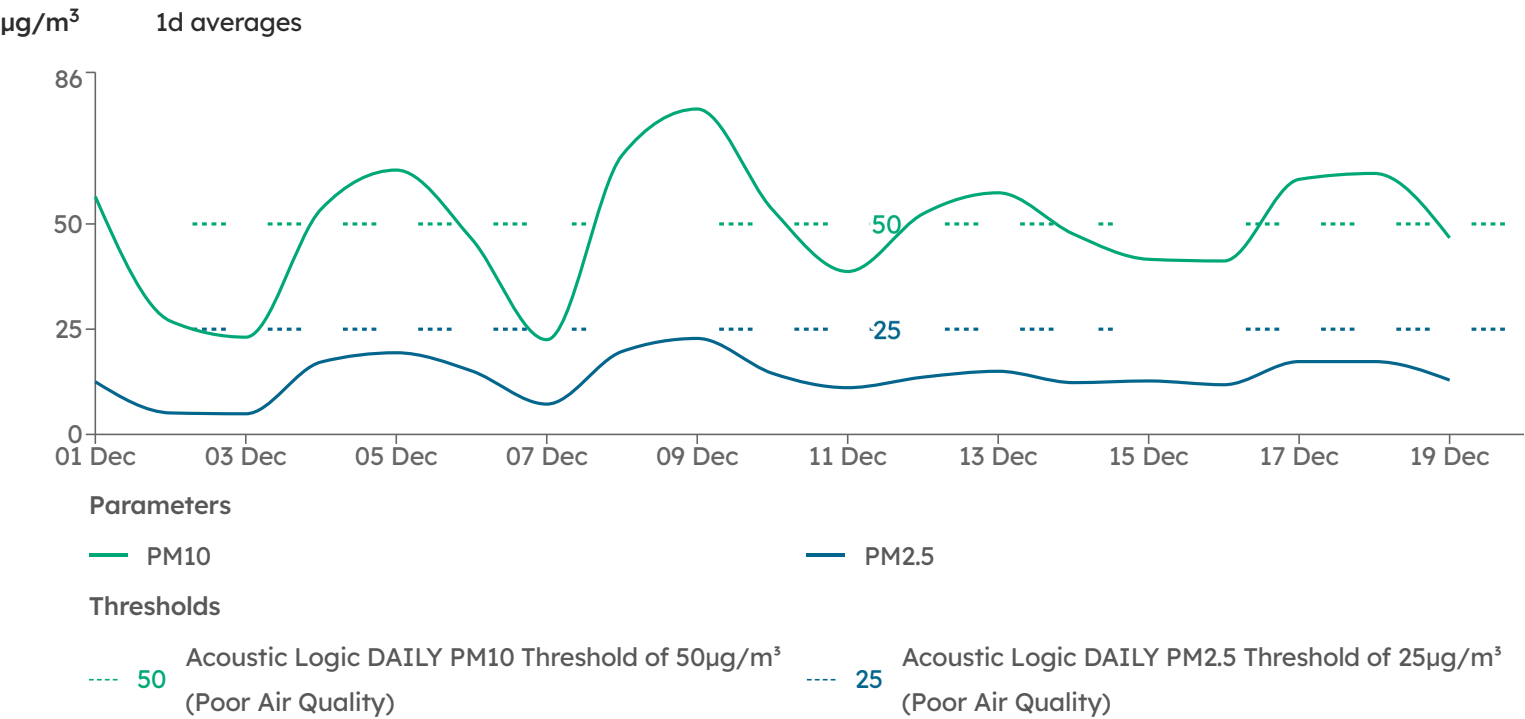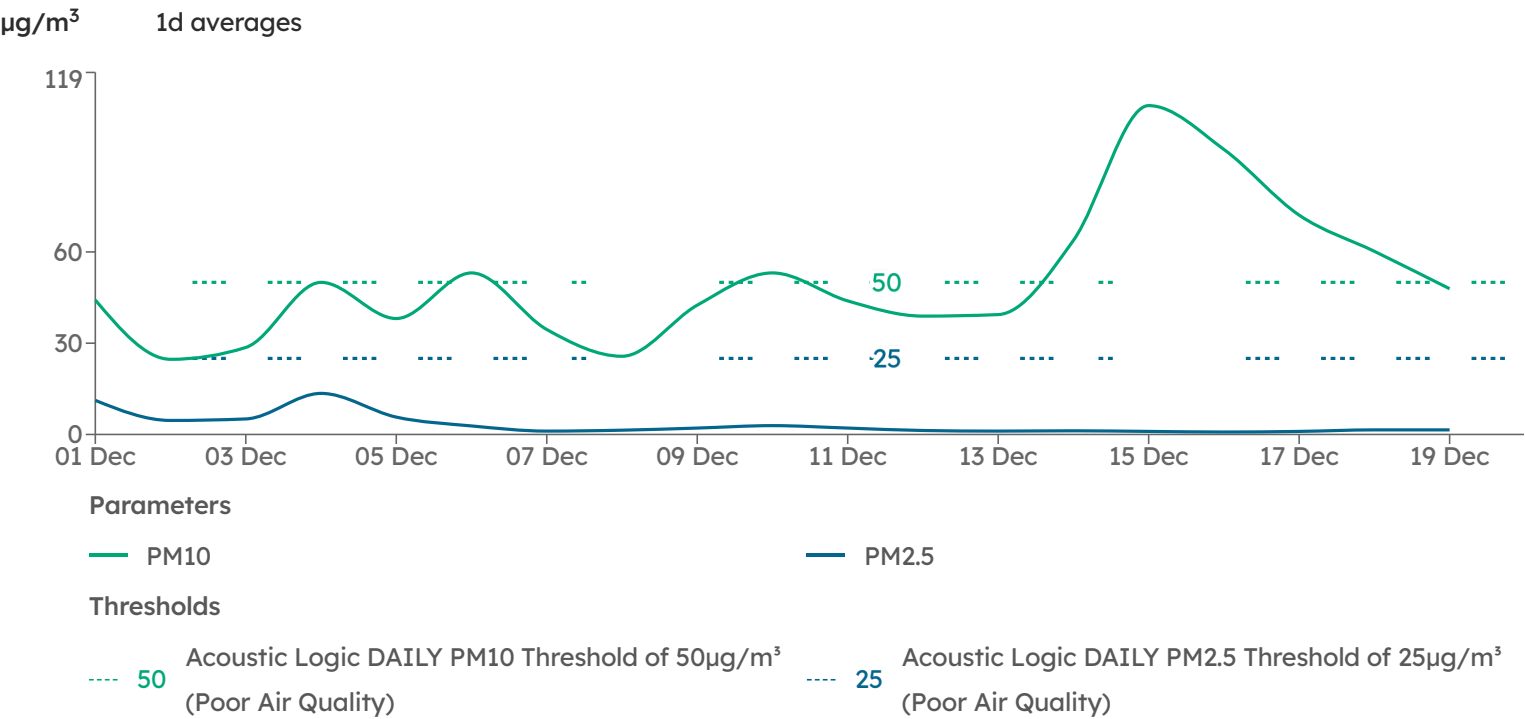

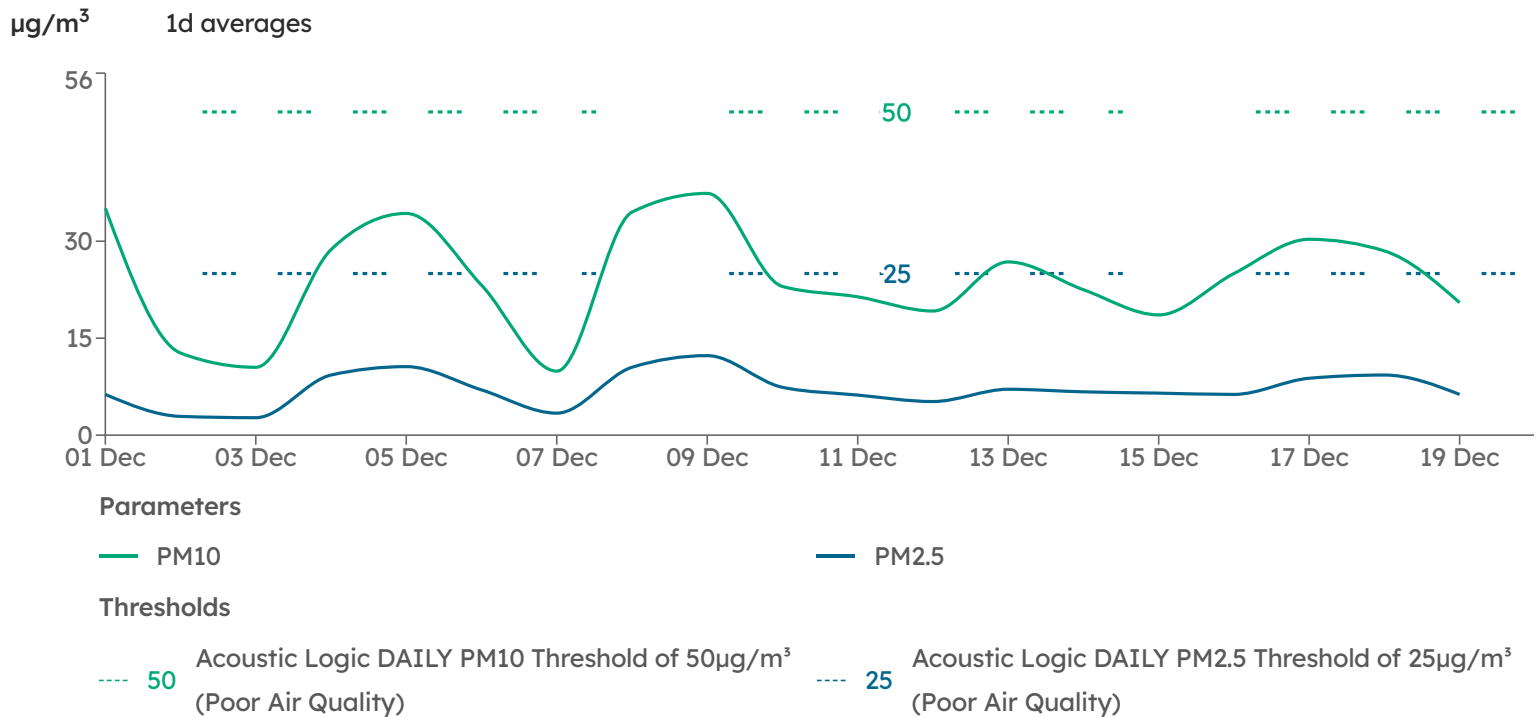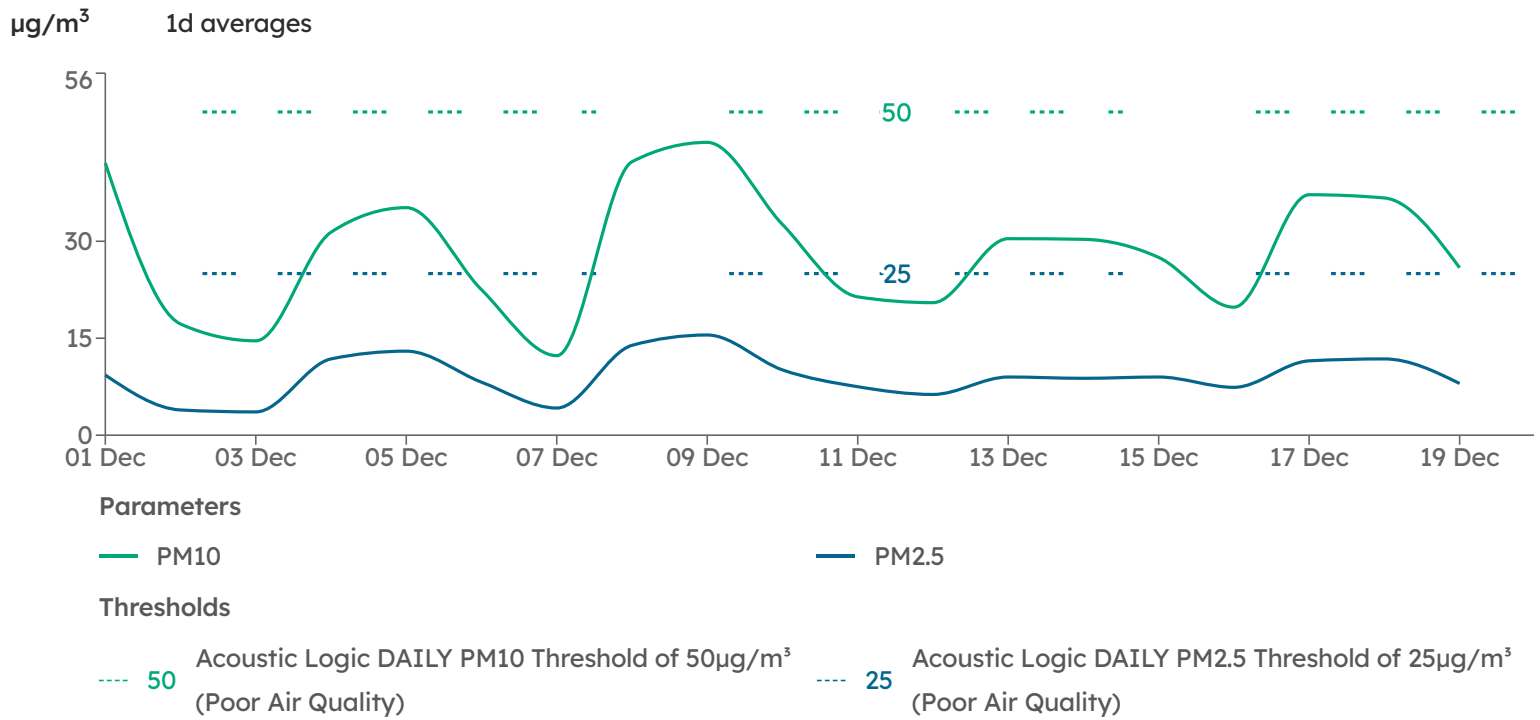

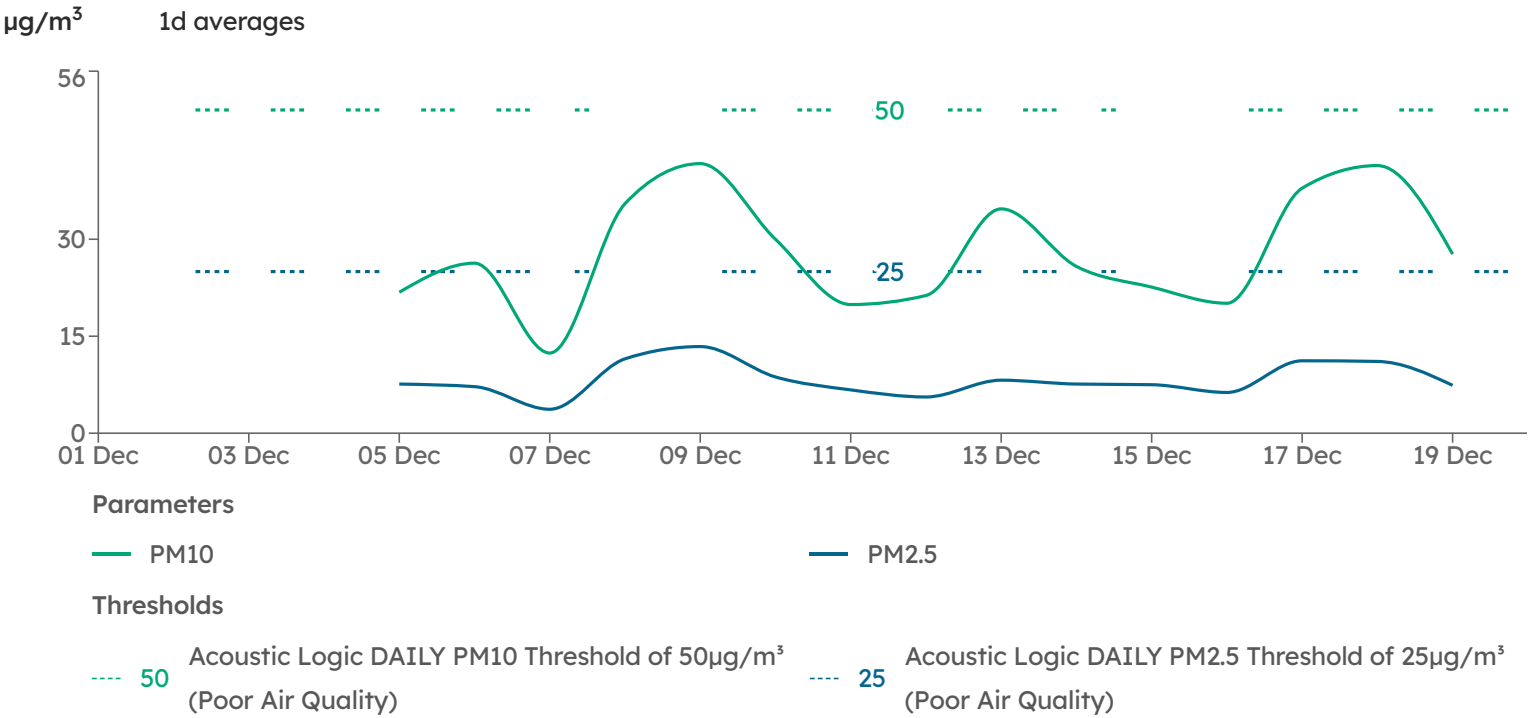

Device Details

Device Serial	Monitoring Points	Model	Calibration Date	Calibration Due
HEX-000171	East Boundary Near Shoalhaven Street	SiteHive Hexanode	03 Apr 2023	03 Apr 2025
HEX-000130	North Boundary Near Block A and B	SiteHive Hexanode	21 Apr 2023	21 Apr 2025
HEX-000232	West of Early Works Zone	SiteHive Hexanode	29 May 2023	29 May 2025
HEX-000401	-	SiteHive Hexanode	16 Aug 2024	16 Aug 2026
HEX-000592	Near Pre-School	SiteHive Hexanode	11 Jun 2024	11 Jun 2026
HEX-000733	Near ICU and Loading Dock	SiteHive Hexanode	13 Nov 2024	13 Nov 2026
