


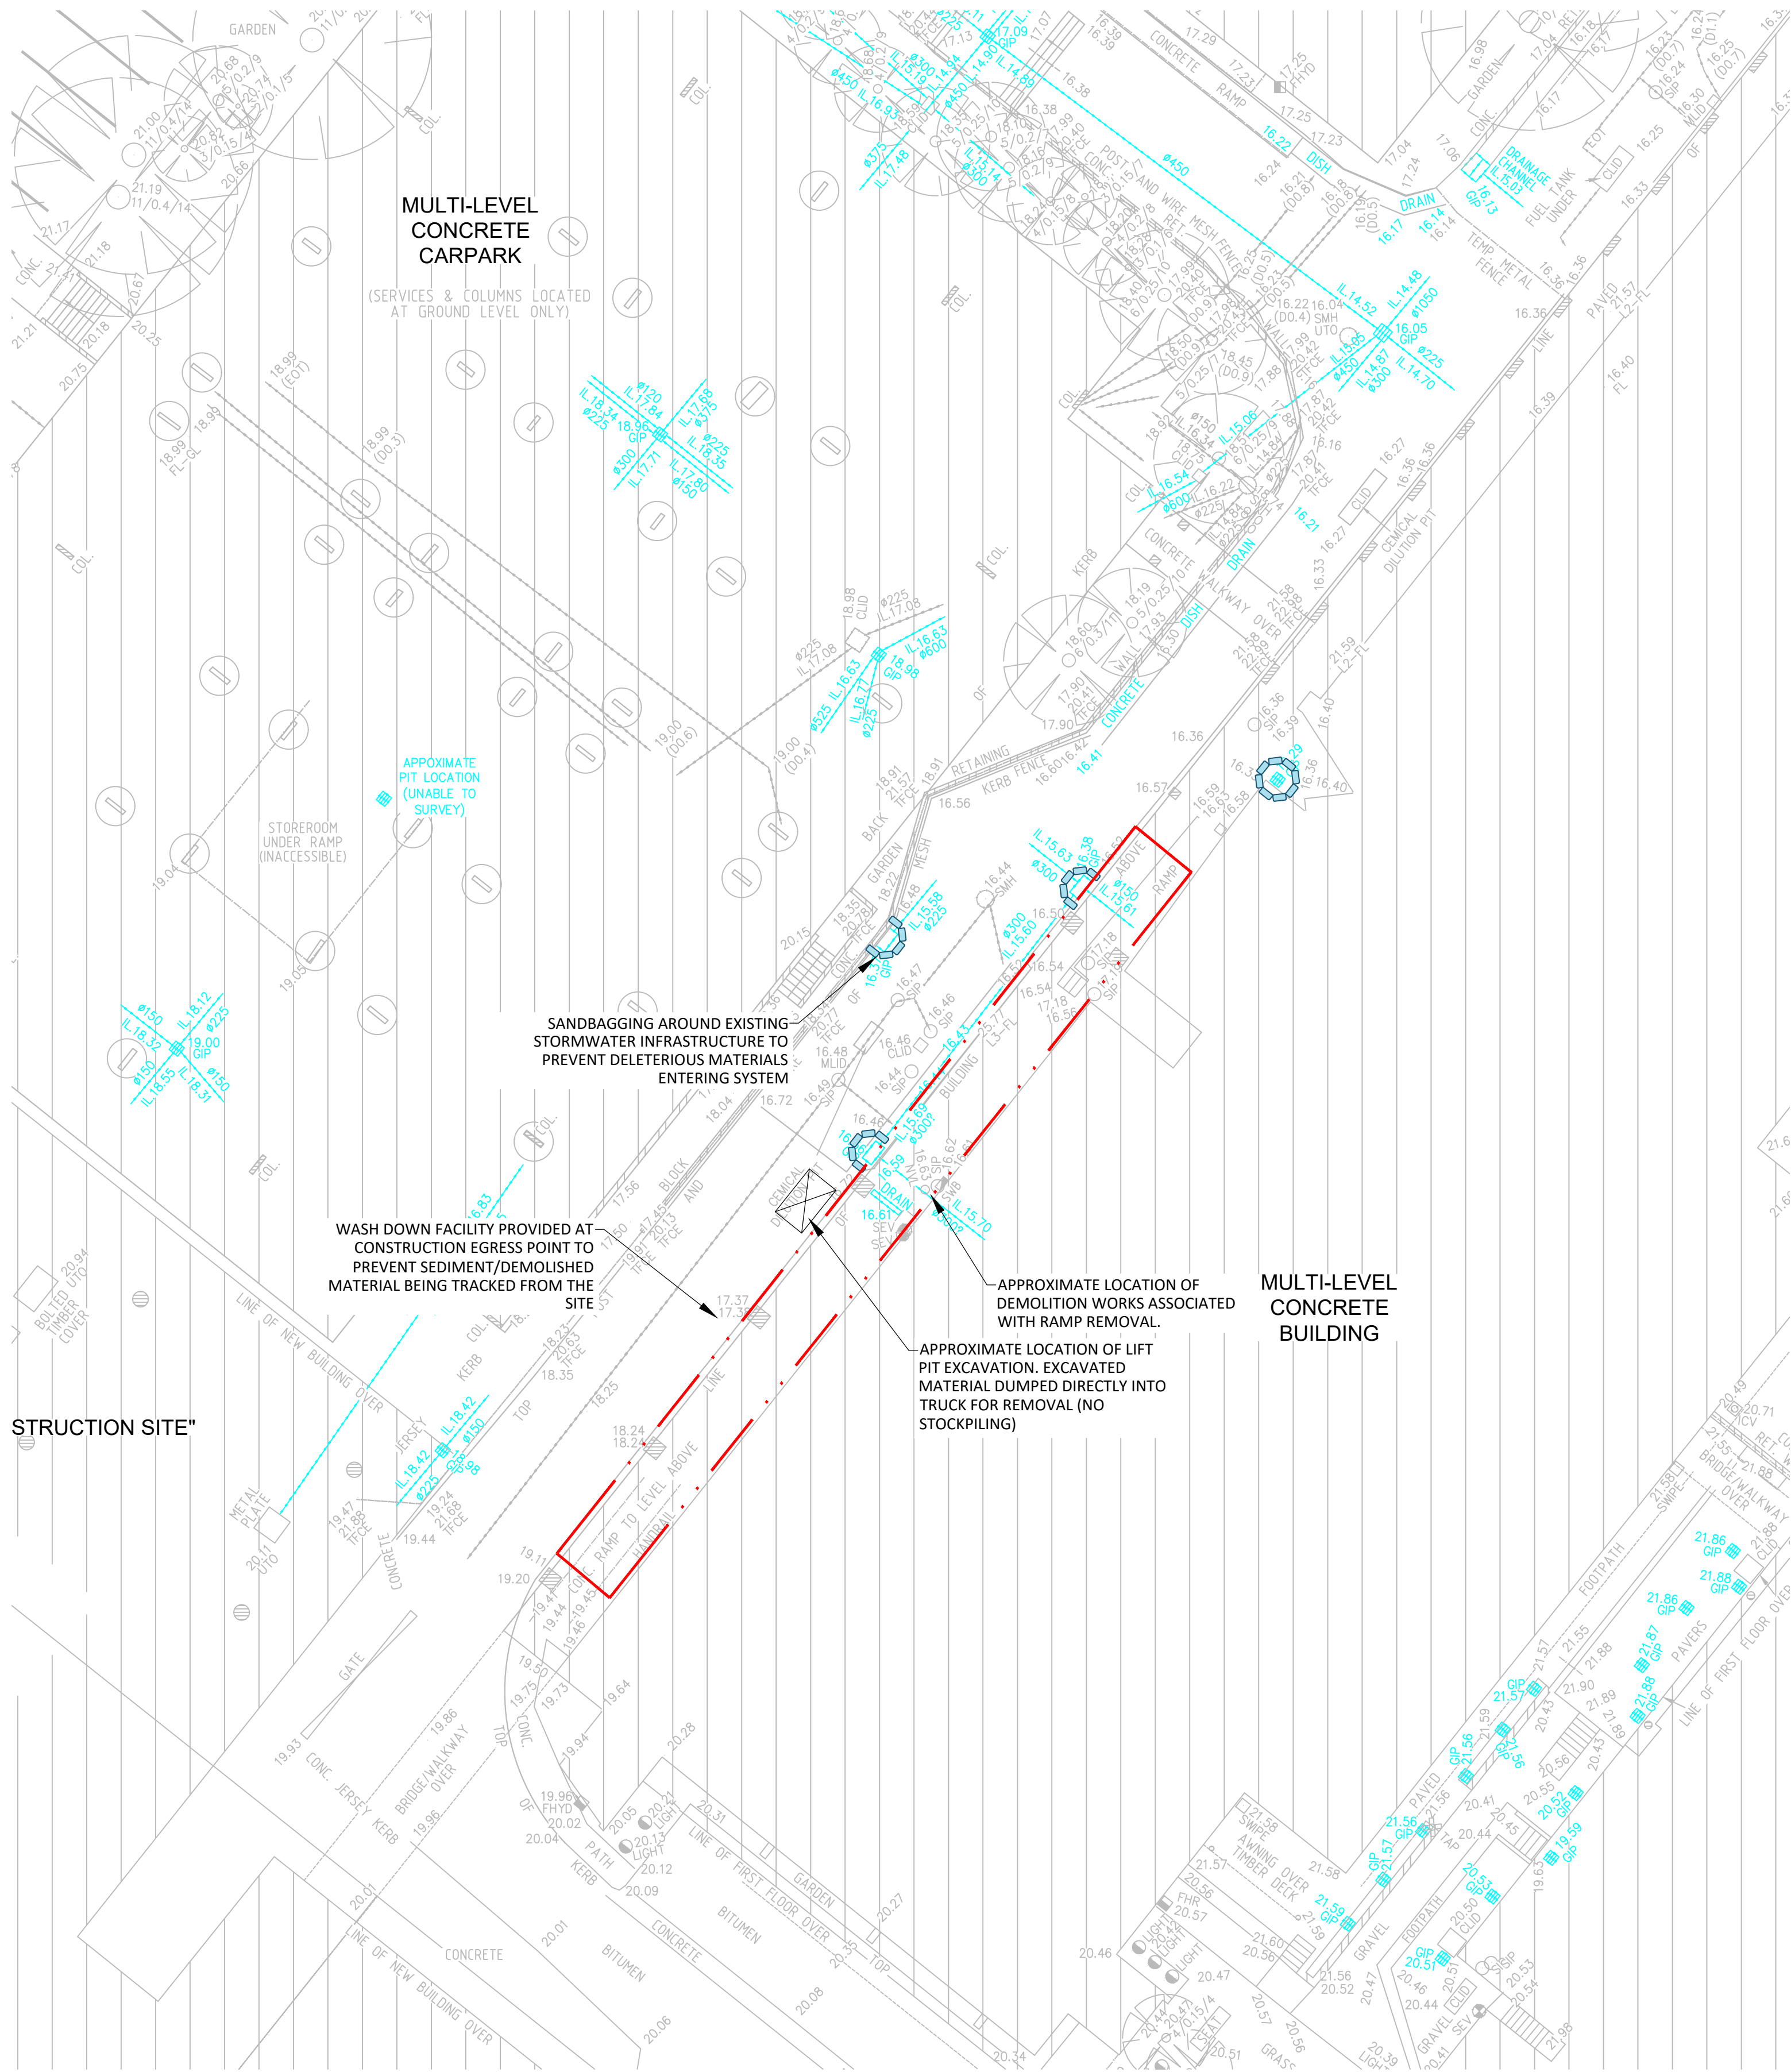


LEGEND

- SITE BOUNDARY
- PROPOSED SANDBAG PROTECTION

EROSION AND SEDIMENT CONTROL NOTES

- ALL WORK SHALL BE GENERALLY CARRIED OUT IN ACCORDANCE WITH:
 - LOCAL AUTHORITY REQUIREMENTS.
 - EPA - POLLUTION CONTROL MANUAL FOR URBAN STORMWATER,
 - DEPARTMENT OF CONSERVATION AND LAND MANAGEMENT MANUAL- "URBAN EROSION & SEDIMENT CONTROL".
- EROSION AND SEDIMENT CONTROL DRAWINGS AND NOTES ARE PROVIDED FOR THE WHOLE OF THE WORKS. SHOULD THE CONTRACTOR STAGE THESE WORKS THEN THE DESIGN MAY REQUIRE TO BE MODIFIED. VARIATION TO THESE DETAILS MAY REQUIRE TO BE APPROVED BY THE RELEVANT AUTHORITIES. THE EROSION AND SEDIMENT CONTROL PLAN SHALL BE IMPLEMENTED AND ADOPTED TO MEET THE VARYING SITUATIONS AS WORK ON SITE PROGRESSES.
- MAINTAIN ALL EROSION AND SEDIMENT CONTROL DEVICES TO THE SATISFACTION OF THE SUPERINTENDENT AND THE LOCAL AUTHORITY.
- MINIMISE THE AREA OF SITE BEING DISTURBED AT ANY ONE TIME.
- PROTECT ALL STOCKPILES OF MATERIALS FROM SCOUR AND EROSION. DO NOT STOCKPILE LOOSE MATERIAL IN ROADWAYS, NEAR DRAINAGE PITS OR IN WATERCOURSES.
- ALL SOIL AND WATER CONTROL MEASURES ARE TO BE PUT BACK IN PLACE AT THE END OF EACH WORKING DAY, AND MODIFIED TO BEST SUIT SITE CONDITIONS.
- CONTROL WATER FROM UPSTREAM OF THE SITE SUCH THAT IT DOES NOT ENTER THE DISTURBED SITE.
- ALL CONSTRUCTION VEHICLES SHALL ENTER AND EXIT THE SITE VIA THE APPROVED CONSTRUCTION ENTRY/EXIT ROUTE.
- ALL VEHICLES LEAVING THE SITE SHALL BE CLEANED AND INSPECTED BEFORE LEAVING.
- MAINTAIN ALL STORMWATER PIPES AND PITS CLEAR OF DEBRIS AND SEDIMENT. INSPECT STORMWATER SYSTEM AND CLEAN OUT AFTER EACH STORM EVENT.
- CLEAN OUT ALL EROSION AND SEDIMENT CONTROL DEVICES AFTER EACH STORM EVENT.

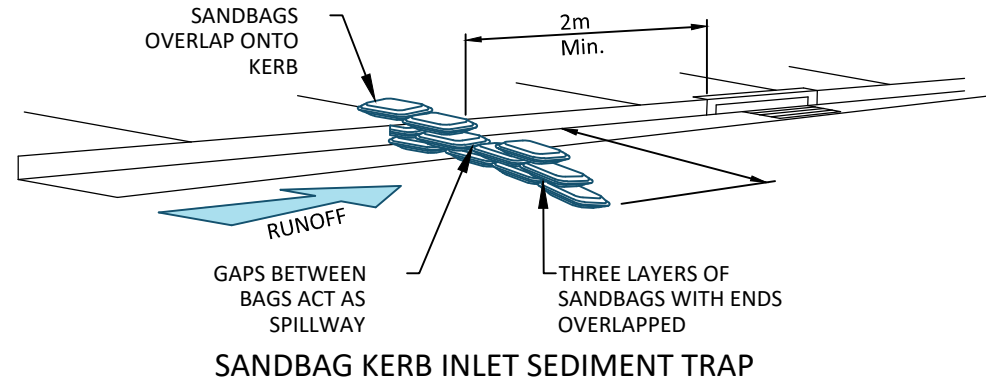

SEQUENCE OF WORKS

- PRIOR TO COMMENCEMENT OF WORKS THE FOLLOWING SOIL MANAGEMENT DEVICES MUST BE INSTALLED:
 - CO-ORDINATE CONSTRUCTION ENTRY/EXIT ROUTES WITH PROJECT MANAGER. ARRANGE SUITABLE LOCATION FOR THE INSPECTION OF TRUCKS PRIOR TO LEAVING SITE AND DIVERT RUNOFF TO SUITABLE CONTROL SYSTEM.
 - PROVIDE SANDBAG SEDIMENT TRAPS UPSTREAM OF EXISTING PITS.
- DISTURBED AREAS ARE TO BE REGULARLY WATERED TO REDUCE DUST POLLUTION.

1:200 2 0 2 4 6 8 10 A1
1:400 A3

REV	DESCRIPTION	DRAWN	APP'D	DATE
A	ISSUED FOR INFORMATION	IH	IH	16.02.23



KANE

CHILDRENS HOSPITAL
WESTMEAD
STAGE 2

SEDIMENT & EROSION
CONTROL PLAN

enscape
studio



PRELIMINARY
NOT FOR CONSTRUCTION

tel 0411 267 151
info@enscapestudio.com.au
ABN 91 649 181 171

AS NOTED	0060-2	C-05	A
SCALE @ A1	PROJECT No	DRAWING No	REV

0060-2-C-05.dwg

22/02/2023 4:45:05 PM

